MMC Build MVP

Development Quotation

Prepared by
Global Buildtech Australia Pty Ltd
ABN 54 672 395 685
For
MMC Build Pty Ltd
Karen Van Den Engel, Founder & CEO

Date: 24 February 2026
Valid for: 30 days from date of issue
Reference: GBTA-MMC-2026-001

COMMERCIAL IN CONFIDENCE

Table of Contents

1. Overview 4
   Technology Stack 4
2. Pricing Summary 5
   R&D Tax Offset 6
   Indicative Timeline 5
3. Stage Deliverables 7
   Stage 0: Project Setup & Foundation — 3 days | $2,550 7
   Stage 1: MMC Comply — NCC Compliance Engine — 20 days | $17,000 8
   Stage 2: MMC Build — Design Optimisation — 15 days | $12,750 9
   Stage 3: MMC Quote — Cost Estimation — 10 days | $8,500 10
   Stage 4: MMC Direct — Trade Directory — 5 days | $4,250 10
   Stage 5: MMC Train — Training Modules — 5 days | $4,250 11
   Stage 6: Billing, Observability & Launch — 3 days | $2,550 11
   Stage 7: Pilot, Iteration & Handover — 10 days | $8,500 12
4. R&D Tax Incentive Evidence Framework 13
5. Payment Schedule 14
6. Platform Running Costs (Not Included) 14
7. Dependencies & Assumptions 15
   Client-Provided Dependencies 15
   Technical Assumptions 15
   R&D Tax Incentive Notes 16
8. Key Risks 16
9. General Terms 17
   Validity 17
   GST 17
   Payment Terms 17
   Intellectual Property 17
   Confidentiality 17
   Scope Changes 17
   Termination 17
   Warranty 17
   Dependencies 17
10. Acceptance 18

1. Overview

This quotation covers the complete design, development, testing, and pilot launch of the MMC Build MVP platform — an AI-powered compliance and construction intelligence platform for the Australian building industry.

The build encompasses all six product modules defined in PRD v3.0, delivered on an optimised Vercel + Supabase + Inngest architecture, with an integrated R&D Tax Incentive evidence framework and a pilot launch to 5–10 firms.

Technology Stack

Layer	Technology	Purpose
Frontend & API	Next.js on Vercel	UI, server actions, API routes — no separate backend server
Database	Supabase PostgreSQL (Sydney)	Relational data, pgvector for RAG embeddings, full-text search
Auth & RBAC	Supabase Auth + Row-Level Security	Multi-tenant authentication and access control
File Storage	Supabase Storage	Plan uploads, generated reports, R&D evidence artifacts
Async Jobs	Inngest	Long-running AI pipelines with retries and step functions
AI / LLM	OpenAI GPT-4 Turbo + Anthropic Claude	Compliance analysis, design optimisation, cost estimation
Payments	Stripe	Subscription billing with 60-day trial
Observability	Vercel Analytics + Sentry	Performance monitoring, error tracking, AI metrics

AU data residency maintained via Supabase Sydney region and Vercel Edge Network. The stack is fully open-source (Next.js, PostgreSQL) with zero vendor lock-in and a clear migration path to AWS for enterprise requirements post-MVP.

2. Pricing Summary

Daily rate: $850 + GST

Total effort: 71 days | Timeline: 14 weeks | R&D eligible: 37 days (52%)

Stage	Weeks	Days	R&D Days	Price (ex GST)
Stage 0: Project Setup & Foundation	1–2	3	1	**$2,550**
Stage 1: MMC Comply — NCC Compliance Engine	2–6	20	14	**$17,000**
Stage 2: MMC Build — Design Optimisation	5–8	15	10	**$12,750**
Stage 3: MMC Quote — Cost Estimation	7–9	10	7	**$8,500**
Stage 4: MMC Direct — Trade Directory	9–10	5	0	**$4,250**
Stage 5: MMC Train — Training Modules	10–11	5	0	**$4,250**
Stage 6: Billing, Observability & Launch	11–12	3	1	**$2,550**
Stage 7: Pilot, Iteration & Handover	12–14	10	4	**$8,500**
TOTAL	**14 weeks**	**71**	**37**	**$60,350**

R&D Tax Offset

Assuming MMC Build Pty Ltd qualifies for the 43.5% refundable R&D Tax Offset (aggregated turnover under $20M). These figures are indicative only — see R&D Tax Incentive disclaimer in Section 7:

	Amount
Quoted price (ex GST)	**$60,350**
GST (10%)	$6,035
Total incl. GST	**$66,385**
R&D eligible spend (37 days × $850)	$31,450
R&D Tax Offset (43.5% of eligible spend)	**– $13,681**
Effective net cost to MMC Build (ex GST)	**$46,669**

Indicative Timeline

The chart below illustrates the 14-week development timeline from a Day Zero starting point. Stages overlap where dependencies allow parallel progress. Total effort is 71 days across 8 stages, with 37 R&D-eligible days (52%).

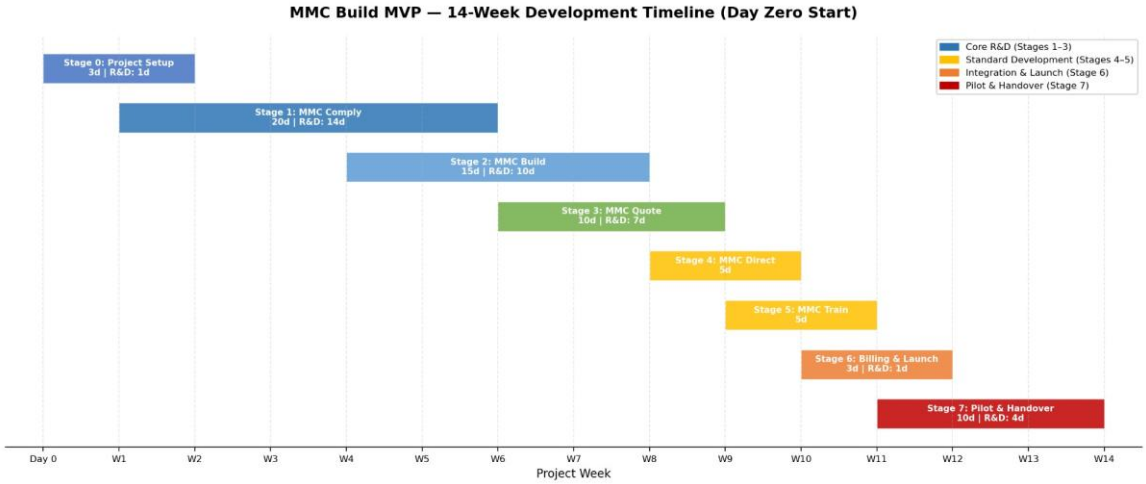

Note: This timeline is indicative and assumes timely provision of all client dependencies (see Section 7). Stage durations represent effort days, not elapsed calendar days. Actual delivery dates will be confirmed upon project commencement and may be adjusted through the agreed change request process.

3. Stage Deliverables

Stage 0: Project Setup & Foundation — 3 days | $2,550

Weeks 1–2 | R&D eligible: 1 day

Deliverable	Description
Supabase project (Sydney)	Database with pgvector. Auth configured. Storage buckets. Row-Level Security for multi-tenancy.
Vercel project + CI/CD	Next.js deployed to Vercel. GitHub auto-deploy. PR preview environments.
Database schema v1	All migrations: tenants, users, roles, projects, plans, reports, feedback, audit_log, R&D evidence tables. RLS enforced.
Authentication & RBAC	Supabase Auth: email + OAuth. JWT tokens. Roles: Owner, Admin, Member, Viewer. Invitation flow.
Application scaffolding	Next.js App Router, Tailwind + shadcn/ui, typed Supabase client, server actions pattern.
Inngest integration	Client connected, webhook endpoint, test function deployed.
R&D evidence infrastructure	Hypothesis register, experiment logger, timesheet tracking, evidence artifact storage, worldwide search log. Database tables and dashboard.

Acceptance Criteria:

- Staging environment accessible and auto-deploying from Git
- Auth flow working: signup, login, invite, role assignment
- Database migrations clean with tenant isolation verified
- R&D evidence tables created and dashboard accessible
- All Stage 1 hypotheses documented before development begins

Stage 1: MMC Comply — NCC Compliance Engine — 20 days | $17,000

Weeks 2–6 | R&D eligible: 14 days (Core R&D)

The primary R&D workstream. AI-powered compliance checking against the National Construction Code using RAG pipeline with citation system.

Deliverable	Description	R&D
Plan upload interface	Drag-and-drop PDF upload. Validation. Supabase Storage with metadata.	—
Document processing pipeline	PDF text extraction, segmentation, OCR. Multi-step Inngest function with Realtime status.	—
NCC knowledge base	NCC Vol 1 & 2 ingestion, chunking, embedding. pgvector storage with clause metadata. 50+ benchmark scenarios.	Core
Embedding pipeline	Vector embeddings via OpenAI. pgvector similarity + full-text hybrid retrieval.	Core
RAG pipeline	Parse → Embed → Query NCC → Generate → Cite. Model routing (GPT-4 / Claude).	Core
Guided questionnaire	Dynamic form: building class, climate zone, site conditions. Responses feed AI context.	—
AI compliance analysis	Multi-pass: structural, fire, accessibility, energy, weatherproofing. Confidence scoring. Low-confidence flagging.	Core
Compliance report	PDF: executive summary, clause-by-clause findings, risk flags, citations. Side panel with NCC references.	—
Feedback & corrections	Thumbs up/down per finding. Free-text corrections for retraining pipeline.	—
Prompt engineering	Model selection logic. A/B testing for prompt variants. Experiment documentation.	Core
Precision benchmarking	Benchmark dataset. Baseline metrics. ≥90% precision target tested and documented.	Core

Acceptance Criteria:

- End-to-end: upload plan → questionnaire → compliance report
- AI precision ≥85% against benchmarks (target 90% by pilot)
- Processing time <2 minutes per plan
- NCC citations traceable to specific clauses
- All R&D experiments logged with observations and metrics

Stage 2: MMC Build — Design Optimisation — 15 days | $12,750

Weeks 5–8 (overlaps Stage 1) | R&D eligible: 10 days (Core R&D)

AI-assisted design optimisation suggesting MMC modifications (prefabrication, SIP systems, panelised construction). Extends Stage 1 RAG pipeline.

Deliverable	Description	R&D
MMC methods knowledge base	Curated dataset: prefab, SIPs, CLT, panelised, modular. Supplier specs embedded for RAG.	Core
Design analysis engine	AI pipeline analysing plans for MMC opportunities. Structured output: suggestion, rationale, impact.	Core
Original vs Optimised view	Side-by-side comparison with annotation layer. Aggregate improvement metrics.	—
Design optimisation report	PDF: recommendations, estimated savings, MMC method references.	—
Accuracy vs expert review	Blind comparison on 5+ plans documented for R&D evidence.	Core

Acceptance Criteria:

- End-to-end: upload plan → optimisation suggestions with rationale
- AI identifies improvement potential in ≥30% of test plans
- Each suggestion includes MMC method reference and estimated impact
- Report exportable as PDF

Stage 3: MMC Quote — Cost Estimation — 10 days | $8,500

Weeks 7–9 (overlaps Stage 2) | R&D eligible: 7 days (Core R&D)

Deliverable	Description	R&D
Supplier knowledge base	Ingestion pipeline for catalogues (PDF, CSV, XLSX). Structured extraction, embedding, indexing.	Core
Cost estimation engine	AI pipeline: map plan elements to materials, retrieve pricing, calculate with confidence bands.	Core
Interactive quote builder	Line items, quantities, costs. User can adjust, swap, override. Summary with confidence band.	—
Quote export	PDF + XLSX: itemised quote, supplier references, assumptions.	—

Acceptance Criteria:

- End-to-end: plan + questionnaire → itemised cost estimate
- Variance ≤15% vs manual quotes (target 10%)
- Line items traceable to supplier sources
- User can adjust items and regenerate totals

Stage 4: MMC Direct — Trade Directory — 5 days | $4,250

Weeks 9–10 | R&D eligible: 0 days

Deliverable	Description
Directory data model	Companies, professionals, certifications, ABN, regions, specialisations, ratings. Seed data.
Profile pages	Company/professional profile: ABN, licences, certifications, service areas, compliance score.
Search & filtering	Category browsing + multi-filter: location, specialty, certification, rating. Full-text search.
Shortlist & contact	Shortlist per project. Send invitation/contact request from profile.

Acceptance Criteria:

- Directory browsable by category with functional filters
- Profile pages render verified company information
- Search returns relevant results within 1 second

Stage 5: MMC Train — Training Modules — 5 days | $4,250

Weeks 10–11 | R&D eligible: 0 days

Deliverable	Description
Course CMS	Courses, modules, lessons, quizzes, enrolments. Admin interface.
Learner interface	Course catalogue, module player, sequential progression, quiz engine.
Progress & certificates	Per-user dashboard, completion tracking, auto-generated PDF certificates.

Acceptance Criteria:

- User can browse, enrol in, and complete a course
- Progress tracked accurately across sessions
- Completion certificate generated as downloadable PDF

Stage 6: Billing, Observability & Launch — 3 days | $2,550

Weeks 11–12 | R&D eligible: 1 day

Deliverable	Description	R&D
Stripe billing	Subscription plans, checkout, customer portal. 60-day trial → paid. Webhooks.	—
Observability	Vercel Analytics + Sentry. AI metrics dashboard. Alerting.	—
AI model observability	Benchmark regression suite. Drift monitoring. Feedback loop pipeline.	Supporting
Security review	TLS enforced. RLS audit. RBAC verification. Audit trail.	—
E2E testing	Integration + UAT test suite across all modules.	—
Pilot launch package	Invite-only onboarding. In-app feedback. Welcome emails.	—

Acceptance Criteria:

- Stripe checkout and subscription lifecycle working
- Observability dashboards live with system and AI metrics
- All core workflows pass end-to-end testing
- Pilot invite flow functional

Stage 7: Pilot, Iteration & Handover — 10 days | $8,500

Weeks 12–14 | R&D eligible: 4 days

Deliverable	Description	R&D
Pilot onboarding	Onboard 5–10 firms. Guided walkthroughs of Comply, Build, Quote.	—
Feedback & iteration	Weekly feedback review. Prioritised bug fixes and UX improvements.	—
AI retraining cycle	Incorporate corrections. Re-run benchmarks. Document outcomes.	Supporting
Post-pilot survey	Structured survey: usability, accuracy, value, willingness to pay.	—
Handover documentation	Architecture docs, deployment runbooks, API reference, operational playbook, backlog.	—
R&D evidence pack	Complete experiment report for AusIndustry. Evidence pack finalised.	Supporting

Acceptance Criteria:

- ≥5 pilot firms actively using the platform
- AI compliance precision ≥90% post-iteration
- ≥60% of pilot users completing 3+ analyses
- Technical documentation complete
- R&D evidence pack ready for AusIndustry registration

4. R&D Tax Incentive Evidence Framework

AusIndustry requires contemporaneous evidence — records created at the time R&D activities occur. This framework is built into the platform from Stage 0, producing evidence automatically as development proceeds.

AusIndustry Requirement	How We Capture It
Hypothesis documented before experiments	rd_hypotheses database table. Created via R&D dashboard before work begins. Timestamped.
Worldwide search / prior art	Documented search log per core R&D activity. Evidence stored in Supabase Storage.
Systematic progression of work	Database enforces chain: hypothesis → experiment → observation → evaluation. All timestamped.
Experiment logs with parameters	rd_experiments: method, parameters, model version, prompt hash, timestamps. Auto-populated by AI pipeline.
Results and observations	rd_observations: precision, recall, confidence metrics, raw outputs. Auto-captured from benchmarks.
Evaluation and conclusions	rd_evaluations: confirmed/refuted/inconclusive, new knowledge, next steps.
Developer timesheets	rd_timesheets: developer, date, hours, R&D activity code, description. Weekly entry.
Evidence artifacts	rd_evidence_artifacts links to files in Supabase Storage. Benchmarks, outputs, git commits.
Evidence pack export	One-click PDF bundle: hypotheses, experiments, observations, evaluations, timesheets, artifacts.

Stage gate R&D checkpoints ensure evidence completeness is verified at each milestone. The evidence pack is audit-ready at all times, not assembled retrospectively.

5. Payment Schedule

Payment	Trigger	Amount (ex GST)	Incl. GST
Deposit (20%)	On acceptance of quotation	**$12,070**	$13,277
Invoice 1 — Stages 0+1	Compliance engine delivered	**$7,480**	$8,228
Invoice 2 — Stages 2+3	Build + Quote delivered	**$21,250**	$23,375
Invoice 3 — Stages 4+5	Directory + Training delivered	**$8,500**	$9,350
Invoice 4 — Stages 6+7	Pilot launch + handover	**$11,050**	$12,155
TOTAL		**$60,350**	**$66,385**

Deposit of $12,070 + GST ($13,277) required upon acceptance. Credited against Stage 0+1 invoice. All invoices payable within 14 days.

6. Platform Running Costs (Not Included)

Ongoing costs incurred directly by MMC Build, separate from development fees:

Service	Est. Monthly Cost	Notes
Vercel Pro	~$20/mo	Hosting, serverless functions, preview deploys, analytics
Supabase Pro (Sydney)	~$25/mo + usage	PostgreSQL + pgvector, auth, storage, realtime
Inngest	$0 (free tier)	25,000 function runs/month
OpenAI API (GPT-4 Turbo)	~$50–200/mo	Primary LLM for AI pipelines
Anthropic API (Claude)	~$20–80/mo	Fallback/comparison model
Stripe	Transaction fees	1.75% + $0.30 per AU card transaction
Sentry	$0 (free tier)	Error tracking and monitoring
Estimated total	**~$95–325/month**	Varies with AI API usage

7. Dependencies & Assumptions

Client-Provided Dependencies

Dependency	Owner	Impact if Delayed
NCC Volume 1 & 2 content (licensed)	MMC Build	Blocks Stage 1
Supplier price lists and specifications	MMC Build	Blocks Stage 3
Sample building plans (PDF) for testing	MMC Build	Degrades AI accuracy testing
Training course content	MMC Build	Blocks Stage 5
Directory seed data (verified trades)	MMC Build	Directory launches empty
5–10 pilot firms confirmed	MMC Build	Blocks Stage 7
Stripe account (test mode)	MMC Build	Blocks Stage 6
Domain, DNS, SSL	MMC Build	Blocks production deploy
UX/UI designs (Figma)	MMC Build / GBTA	Functional UI provided if not supplied
Stage gate approvals	MMC Build	≤5 business days per gate

Technical Assumptions

- Single full-stack developer (GBTA) delivering all stages
- TypeScript (Next.js) for all code — no separate Python backend
- Supabase Pro with Sydney region for AU data residency
- Vercel Pro for production hosting
- OpenAI GPT-4 Turbo as primary LLM; Anthropic Claude as fallback
- Inngest for async AI pipeline orchestration
- pgvector on Supabase for embeddings (no separate vector DB)
- 3D viewer is stretch goal; may be descoped to 2D overlay
- LLM API costs billed separately or passed through
- R&D documentation maintained contemporaneously throughout
- Estimates assume no scope changes; change requests via agreed process

R&D Tax Incentive Notes

- All development by AU-resident developers under GBTA (ABN 54 672 395 685)
- MMC Build is the R&D entity and claimant; GBTA is contracted provider
- Timesheets tracked against R&D activity codes from commencement
- $850/day reflects market rate for senior AI development (arm's length pricing)
- R&D offset figures are indicative — engage an R&D tax advisor before lodging
- R&D activities must be registered with AusIndustry within 10 months of FY end

Important Disclaimer — R&D Tax Incentive: All R&D Tax Incentive figures, eligible day allocations, and offset calculations presented in this quotation are indicative estimates only and do not constitute tax, legal, or financial advice. Eligibility for the R&D Tax Incentive is determined by the Australian Taxation Office (ATO) and AusIndustry based on the specific circumstances of the claimant entity. MMC Build Pty Ltd should obtain independent professional advice from a qualified R&D tax advisor and/or registered tax agent before relying on any R&D offset figures, lodging an R&D Tax Incentive registration, or making any financial decisions based on the estimated offset amounts. GBTA accepts no liability for the accuracy of R&D eligibility assessments or offset calculations, and actual outcomes may differ materially from the estimates provided.

8. Key Risks

Risk	Impact	Mitigation
NCC content licensing	Blocks Stage 1 entirely	Client to confirm access before Stage 1 begins
AI accuracy below 90%	Undermines trust and PMF	Iterative prompt engineering; human-in-the-loop; pilot tuning
3D viewer complexity	Ambitious for MVP	Descope to 2D overlay; defer 3D to Phase 2
Supplier data quality	Reduces quoting accuracy	Structured ingestion with validation; confidence bands
Scope creep (6 modules)	Diluted quality risk	Stage gates; Comply prioritised as wedge product
R&D documentation gaps	ATO rejection risk	Automated evidence capture; stage checkpoints; advisor review

9. General Terms

Validity

This quotation is valid for 30 days from the date of issue (24 February 2026).

GST

All prices exclusive of GST. GST of 10% added to all invoices.

Payment Terms

Invoiced per payment schedule. Payable within 14 days. 20% deposit ($12,070 + GST) required to commence.

Intellectual Property

All code, documentation, and artifacts are the property of MMC Build Pty Ltd upon payment. GBTA retains the right to use general knowledge, techniques, and non-client-specific methodologies.

Confidentiality

Both parties maintain confidentiality of all proprietary information shared during the engagement.

Scope Changes

Changes documented via written change request with impact assessment and approval before work commences.

Termination

Either party may terminate with 14 days written notice. GBTA invoices for all work completed to date.

Warranty

30-day warranty following Stage 7 handover for defects against agreed acceptance criteria. New features not covered.

Dependencies

Timeline assumes timely provision of all client dependencies. Delays may extend the timeline.

10. Acceptance

To accept this quotation, please sign below and return to:

Dennis McMahon
Global Buildtech Australia Pty Ltd
ABN 54 672 395 685
E: dennis@corporateaisolutions.com
M: +61 402 612 471

Accepted by: _____

Name: _____

Position: _____

Date: _____

Signature: _____
